RESERVED
AS NOTED

KEY:

ZONE KNOWN TO REQUIRE CHANGES
AS DESIGN MATURES

GENERAL NOTES

1. PORTABLE EQUIPMENT AND ALTERNATE EQUIPMENT LOCATIONS SHOWN IN LIGHT GRAY.

REVISIONS

REV	SH	ZONE	ITEM	DESCRIPTION	DATE	APPVL SIG & ORG
–	ALL	ALL	–	INITIAL ISSUE THIS DOCUMENT UPDATES THE CONTRACT DRAWING GENERAL ARRANGEMENTS, DRAWING NO. 12100-070-01, REV A, DATED 7/29/16 WITH FOLLOWING CHANGES:	11/16/17	JBB/G&C
	4	8B	1	REMOVED REFERENCE TO 'THRUSTER LUBE OIL TANK'		
	4	4B	2	REMOVED CLEANING GEAR LOCKER		
	4	3B	3	ADDED HORIZONTAL WT BOUNDARY, CHANGED ROOM NUMBER TO BOW THRUSTER VOID 4-5-0 AND EXTENDED GRATING TO AFT END OF BOWTHRUSTER ROOM		
	4	2B	4	ADDED INSPECTION ACCESS TO VOID (2-(-2)-0		
	6	2B	5	MOVED HATCH TO BE CENTERED ON FRAME 11.5		
	7	3D	6	MOVED HATCH TO BE CENTERED ON FRAME 11.5		
	8	4D	7	REMOVED ROOM NUMBER FROM WORK SHOP AREA		
	8	4C	8	CHANGED ROOM NUMBER TO 3-31-0		
	8	3C	9	EXTENDED GRATING TO AFT END OF BOW THRUSTER ROOM, CHANGED DEPICTION		
	8	2D	10	ADDED INSPECTION ACCESS TO VOID (2-(-2)-0 (REVISIONS CONTINUE ON SEE SHEET 1A)		

REFERENCE PLANS

NO.	TITLE	DRAWING NUMBER
25	PORT TRANSDUCER POLE	M015736
24	SEA CHEST ARRANGEMENTS	6096-163-001
23	EMERGENCY TOWING PLAN	6096-500-003
22	ANCHOR HANDLING & MOORING FOUNDATIONS	6096-581-001
21	ALUMINUM SUPERSTRUCTURE ARRANGEMENT	6096-150-001
20	BROW DESIGN AND STORAGE	6096-616-002
19	PROVISION COOLING PLANT (HEINEN & HOPMAN)	32817023-601
18	CHILLER (HEINEN & HOPMAN)	32817023-401
17	ANCHOR WINCH RIGHT VERSION	RH321674
16	ANCHOR WINCH LEFT VERSION	RH321675
15	PORTABLE WINCH (RAPP)	RH324106
14	PORTABLE OFFSHORE FOLDABLE TELESCOPIC CRANE (RAPP)	MG-FT005D-S2
13	HYDROGRAPHIC WINCH (RAPP)	RH324104
12	MAIN A-FRAME STERN (RAPP)	18729
11	PORTABLE A-FRAME SIDE (RAPP)	17864
10	CTD DAVIT (RAPP)	17844
9	OFFSHORE FOLDABLE TELESCOPIC CRANE – MAIN DECK (RAPP)	MG-FT020DH-S3
8	PILOTHOUSE & CHART ROOM ARRANGEMENT	6096-661-001
7	MACHINERY ARRANGEMENT	6096-500-001
6	HEATING, VENTILATION & AIR CONDITIONING SYSTEM	6096-512-001
5	FREEING PORT ARRANGEMENT & DETAILS	6096-190-001
4	OVERBOARD HANDLING SYSTEMS	6096-710-001
3	MOORING ARRANGEMENT	6096-580-001
2	LINES PLAN	6096-070-002
1	TECHNICAL SPECIFICATION	12100.05

SPECIAL NOTATIONS

THIS DRAWING IS A LIVE DOCUMENT AND REFLECTS LATEST DESIGN DATA AS NOTED. SEE REFERENCES FOR INFORMATION.

DRAWING CONFIDENTIALITY STATEMENT

THIS DRAWING IS TO BE USED FOR CONSTRUCTION OF THE REGIONAL CLASS RESEARCH VESSELS. USE AND/OR REPRODUCTION OF THIS DRAWING AND FURTHER DISSEMINATION IS AUTHORIZED ONLY AS DIRECTED BY GULF ISLAND SHIPYARDS OR OREGON STATE UNIVERSITY.

PROFESSIONAL ENGINEER STAMP

GULF ISLAND SHIPYARDS
301 GULF ISLAND ROAD
HOUMA, LA 70363
PHONE: (985) 872-2305
CONTRACT/PO NO.
184162

DRAWN: J. PIZZITOLA	01/12/18	
CHECKED: G. MCCANN	01/12/18	
APPROVED: C. FLY	01/12/18	

C.FLY MARINE SERVICES, LLC.
NAVAL ARCHITECTS & MARINE ENGINEERS
WWW.CFLYMARINE.COM
HOBE SOUND FL

OREGON STATE UNIVERSITY
CORVALLIS, OR 97331

199'-6" REGIONAL CLASS RESEARCH VESSEL
GENERAL ARRANGEMENT
COVER SHEET

SIZE	FSCM CAGE NO.	DRAWING NO.	REV
D	7UTH5	6096-070-001	J

SCALE: NONE | HULL #: 6096 6097 6098 | SHEET 1 OF 10

REVISIONS CONTINUED

REV	SH	ZONE	ITEM	DESCRIPTION	DATE	APPVL SIG & ORG
	4	7B	11	CHANGED ROOM NUMBER 3-86-0 TO 3-85-0		
	4	5B	12	CHANGED 'DRY PIT' TO 'GRAY WATER'		
	4	3B	13	CHANGED 'HVAC EQUIPMENT ROOM' TO 'GARBAGE ROOM'		
	8	7C	14	CHANGED ROOM NUMBER 3-86-0 TO 3-85-0		
	8	5B	15	ELIMINATED DRY PIT AND ADDED CL BLKHD BETWEEN GW TANK AND BALLAST TANK		
	8	3B	16	CHANGED ROOM NUMBER TO BOW THRUSTER VOID 4-5-0		
	4	2C	17	ADDED DECK LOCKER 01-(-4)-0 TO INBD PROFILE		
	7	5B	18	FIXED ROOM NUMBER TEXT MASKING		
	1A	ALL	19	ADDED SHEET 1A		
	3	5B,6B	20	SHIFTED WINDOWS AFT CENTERED ON FRAME		
	7	3D,4D				
	ALL	ALL	21	REVISED ANCHOR WINCHES PER REF 17 & 18		
	ALL	ALL	22	REVISED MOORING EQUIPMENT PER REF 4		
	ALL	ALL	23	ADDED FREEING PORTS PER REF 6		
	ALL	ALL	24	ADDED DECK WINCHES PER REF 15		
	ALL	ALL	25	REVISED MAIN A-FRAME (STERN) PER REF 12		
	6	3D	26	ADDED HINGED OPENING TO CHART ROOM		
	4	2C	27	ADDED LADDER HANDRAIL		
	8	3B	28	REVISED DECK TO SUIT BOW THRUSTER VOID		
	8	4D	29	REVISED PROVISION COOLING PLANT PER REF 18		
	8	6B	30	REVISED SPACE DESIGNATION		
	8	4B	31	REMOVED REFERENCE TO TRUNK		
	8	7C	32	UPDATED WINCH ROOM EQUIPMENT		
	ALL	ALL	33	REVISED PORTABLE A-FRAME PER REF 12		
	ALL	ALL	34	REVISED CTD DAVIT PER REF 10		
	8	5C	35	REVISED CHILLER PER REF 19		
	ALL	ALL	36	REVISED FLAG SHEAVE		
	8	7D	37	REVISED OVERHEAD HATCH DEPICTION		
	ALL	ALL	38	UPDATED DRAWING NUMBER		
	1	1-B	39	UPDATED REFERENCE DRAWING NUMBERS		
P1			–	REVISION TO INCORPORATE OSU AND GIS COMMENTS	01/11/18	JP/FLY
	2	7B	1	REVISED A-FRAME TO SHOW ONE VIEW		
	ALL	ALL	2	REVISED CRANE TO SHOW ONE VIEW		
	ALL	ALL	3	MODIFIED EXHAUST STACK FOR RESCUE BOAT		
	ALL	ALL	4	ADDED FREEING PORTS PER REF 5		
	7	6D	5	RESERVED BROW DESIGN		
	4	5B	6	RESERVED ENGINE FOUNDATION PENDING CAT		
	4	3B	7	RESERVED BOW THRUSTER FOUNDATION		
	8	7C,7D	8	MODIFIED BHD 85-86 FOR Z-DRIVE PLACEMENT		
	8	ALL	9	MODIFIED HOLD ARRANGEMENT TO SUIT CHANGES		
	4	6B	10	MODIFIED WINCH ROOM DECK FLAT HEIGHT		
	4	5B	11	MODIFIED ENGINE ROOM DECK FLAT HEIGHT		
	5	3B,6B	12	MODIFIED END VIEWS TO SHOW DECK HEIGHTS		
	7	7A	13	RESERVED SIDE A-FRAME PENDING RAPP		
	6	3B	14	REMOVED ONE AHU RESERVED PENDING LEBLANC		
	8	3C	15	ADDED MCC#1 IN SHIP STORES		
	ALL	ALL	16	REPLACED RESCUE BOAT AND DAVIT		
	4	2B	17	MOVE FLAT OF VOID TO 12' ABL		
–			–	REVISION TO INCORPORATE OSU COMMENTS	02/08/18	KS
	8	3D,6B 6D,7D	1	UPDATED TANK TOP OUTLINES @ HOLD PLAN & TANK TOP PLANS		
	8	6D	2	DELETED STEPS.		
	7	6A,6C	3	RELOCATED STAIRS INBOARD 8" TO CLEAR BERP.		
	7, 2,3	6B,7B 6B,2B	4	UPDATED REMOVABLE BULWARKS AND MOORING BITS, MAIN DECK AFT PER REF 4		
	4, 5 6	5B, 4B, 5B	5	UPDATED STACK		
	3	4C	6	REVISED SIDE OPENING PER REF 21		
	2	4C	7	REVISED DECK HOUSE SIDE BHD PER REF 21.		
	2	7B	8	ADDED SIDE A-FRAME.		
	4	5B,5C	9	INDICATED EXHAUST PIPE CL ELEVATION		
	7	5B	10	UPDATED SCR MODULE.		
	8	7D	11	UPDATED WINCH ELECTRICAL CABINET SIZE.		
	6, 7	8C,8D 7B	12	DELETED MANHOLES ON MN DK INTO AFT PEAK.		

REVISIONS CONTINUED

REV	SH	ZONE	ITEM	DESCRIPTION	DATE	APPVL SIG & ORG
	7	5A	13	DELETED EXTRANEOUS CTD POSITIONS.		
	7 8	3B 3C	14	RELOCATED BOW THRUSTER RM MANHOLE.		
	2	6A	15	ADDED ELEVATION 2-6A.		
	6 7	5B 5D	16	MODIFIED BHD IWO OF BOAT.		
	7	7B	17	REVISED STERN A-FRAME STOWED POSITION.		
	8	5C	18	REMOVED MINOR MACHINERY THRUOUT HOLD.		
	8	6C	19	UPDATED ELECTRICAL EQUIPMENT.		
	2	4B	20	UPDATED 01 LEVEL FREEING PORTS.		
A	ALL	ALL	21	INCREASED VESSEL LENGTH BY 6'-0".	6/14/2018	
	8	4D		INCREASED LENGTH OF DOMESTIC EQUIP. ROOM BY 4'.1st PLATF FR 31-FR 41.		
	8	5D		INCREASED AUX MACH RM LENGTH BY 2', 1st FLATF FR 41-51		
	8	5B		INCREASED LENGTH OF THE U-TUBE ROLL TK BY 2', 1st PLATF FR 37-41.		
	8	4D	22	REMOVED STATEROOMS, 1st PLATF FR 22-31.		
	8	4D	23	RELOCATED SLIDING WT DOOR 1st PLATF FR 22.		
	8	4D	24	RELOCATED GYM TO 1st PLATF FR 22-31 CL.		
	8	4D	25	RELOCATED WORKSHOP 1st PLATF TO FR 22-31 PORT SIDE.		
	8	5C	26	REVISED POT WTR TKS, 1st PLATF FR 37-41.		
	8	5D	27	MOVED CENTERBOARD FWD 2'.		
	8	5D	28	REVISED TKS P&S OF CENTERBOARD.		
	8	5C	29	REVISED MACHINERY PER LENGTHENED MACHINERY ARRANGEMENT.		
	8	5B	30	DIVDED FO TK 4C INTO PORT AND STBD TKS.		
	8	5B	31	MOVED GREY WTR OUTBD, FO 5P INBD.		
	8	5B	32	MOVED FO SETTLING TK FWD OF FR 51.		
	8	5A	33	MOVED FO 5S INBD, BALLAST 5S OUTBD.		
	8	6B	34	DELETED BALLAST 6AC, EXTENDED FO 6 P&S AFT TO FR 67.		
	8	6A,6B	35	DELETED VOID 6A P&S, EXTENDED BALLAST 6 P&S AFT TO FR 63.		
	7	3B	36	LENGTHEND MESS DECK BY 2', FR 23-24.		
	7	5B	37	LENGTHEND FAN RM BY 4', FR 48-57 , MN DK.		
	7	4B,4D	38	MOVED FIRE SUPPRESSION RM FROM 01-45-4 TO 1-48-4.		
	7 8	3B, 4D	39	RELOCATED HATCHES MAIN DK & 1ST PLATFORM TO FR 26, 3'-7" TO PORT SIDE.		
	7	5B	40	LENGTHEND WET LAB AND SIDE DECK BY 6'.		
	2,3, 4,5	ALL	41	ADDED 6" HEIGHT BETWEEN 01 AND 02 LEVEL.		
	7	4C	42	MOVED HOSPITAL FROM PORT TO STBD SIDE.		
	7	3C,4D	43	SPLIT 01 LEVEL HVAC RM INTO 2 ROOMS, P&S.		
	7	4D	44	MOVE LAUNDRY FROM STBD TO PORT SIDE. ADD SEPERATE CG LKR STBD.		
	7	4D	45	ADDED BREEZEWAY PORT SIDE FR 47-50. RESIZED TECH LKR.		
	7	5B	46	REVISED BOSUN STORE/SHOP & DC LKR.		
	7	3C,4C	47	MOVED 2 CREW STATEROOMS TO 01 LEVEL FR 29-39 PORT SIDE.		
	6	4B	48	MOVED 3RD MATE & 3RD ENGINEER STATEROOM TO 02 LEVEL FR 33-41 PORT SIDE.		
	7	8B	49	ADDED ALTERNATE WINCH ARRANGEMENT.		
	2	7D	50	UPDATED VESSEL PARTICULARS TABLE.		
	2,3, 4,5	VAR	51	UPDATED MAST.		
	2, 2, 5, 7	5C, 5A, 3B, 5B	52	RAISED 01 LEVEL 18". FRAME 52 AFT, STBD SIDE, 10' OCL TO SIDE SHELL.		
B	2	–	18	REVISED VESSEL PARTICULARS, UPDATED AIR DRAFT MEASUREMENT.	7/30/18	GM/CFF
	2	5A, 6A	17	UPDATED BULWARK ARRANGEMENT TO SUIT FORWARD & AFT LOCATIONS OF SIDE MOUNTED A-FRAME.		
	2	5A	16	UPDATED FORWARD FORWARD MAST.		
	2	5A	15	UPDATED ANTENNA ARRANGEMENT.		
	3	4A	16	UPDATED FORWARD FORWARD MAST.		
	3	4A	15	UPDATED ANTENNA ARRANGEMENT.		
	4	5A	14	UPDATED ANTENNA ARRANGEMENT.		
	5	3A, 6A	13	UPDATED ANTENNA ARRANGEMENT		

REVISIONS CONTINUED

REV	SH	ZONE	ITEM	DESCRIPTION	DATE	APPVL SIG & ORG
B	6	7C	13	UPDATED DECK TIE-DOWN ARRANGEMENT.	7/30/18	GM/CFF
	6	3C	12	UPDATED BROW TO SUIT CURRENT DESIGN.		
	6	3C	11	ADDED "BERP" TO TOP OF CENTERBOARD TRUNK ASSEMBLY.		
	6	3A	10	ADDED DOOR TO CENTERBOARD CUTOUT ON PORT SIDE.		
	6	3A	19	REVISED STACK BULKHEADS TO SUIT MODEL.	7/31/18	GM/CFF
	7	8B	9	UPDATED ARRANGEMENT OF CTD WINCHES, FOR SIDE A-FRAME, FORWARD LOCATION		
		5C	9	UPDATED ARRANGEMENT OF CTD WINCHES, FOR SIDE A-FRAME, AFT LOCATION		
	7	2C 2D	8	UPDATED ANCHOR WINDLASS FOUNDATIONS, AND MOORING ARRANGEMENT.		
		5A	7	UPDATED BULWARK IN WAY OF SIDE A-FRAME, FORWARD & AFT LOCATIONS.		
		5A	6	REVISED JOINER BULKHEADS, PORT LONGITUDINAL BULKHEAD ADJACENT TO CENTERBOARD TRUNK.		
		5A	5	REVISED STIFFENER LOCATIONS ON TRANSVERSE BULKHEAD AT FR 14, TO AFT SIDE OF THE BULKHEAD. FR 21 (PORT SIDE), STIFFENERS ARE NOW SHOWN ON THE FORWARD SIDE.		
		5A	20	REVISE EXHAUST STACK BULKHEADS TO SUIT MODEL	7/31/18	GM/CFF
	8	5C	4	UPDATED WINCH ROOM ARRANGEMENT.		
		5C	3	REMOVED FOR DRAWING CLARITY, ALL NON-ESSENTIAL MACHINERY FROM VARIOUS MACHINERY SPACES.		
		5A	2	ADDED LOCATION FOR SCIENCE SERVICES SEACHEST.		
		5A	1	ADDED LOCATION FOR FORWARD FIRE MAIN SEACHEST, IN BOW THRUSTER VOID.		
	VAR	VAR	21	UPDATED FURNITURE THRU-OUT PER MIS DRAWING #41265-004	8/03/18	KS
	VAR	VAR	22	UPDATED T&S UNITS PER VENDOR INFO.	8/20/18	KS
	6 7	5B 4B,4D	23	ADDED VENTILATION TRUNK 1-50-2.		
	2 3 4 6	5B,5C 4C 5C 5D,8D	24	REVISED STACK.		
C	1	–	1	UPDATED TITLE BLOCK PER OSU COMMENTS	10/15/18	GM/CFF
	2	5A, 6A	2	UPDATED FREEING PORTS PER FREEING PORT ARRANGEMENT. UPDATED FORWARD MAST TO SUIT CURRENT ARRANGEMENT. UPDATED ALL RAPP EQUIPMENT.		
	3	4A	3	UPDATED FORWARD MAST TO SUIT CURRENT ARRANGEMENT. UPDATED ALL RAPP EQUIPMENT.		
	4	5A	4, 5, 6, 7,	UPDATED FORWARD MAST TO SUIT CURRENT ARRANGEMENT. UPDATED FORWARD BOW THRUSTER ARRANGEMENT. ADDED SONAR CASINGS LOCATED AT CENTERLINE. UPDATED ALL RAPP EQUIPMENT.		
	5	3A	8	UPDATED ALL RAPP EQUIPMENT.		
	6	3A	9, 10	UPDATED ARRANGEMENT TO SUIT REVISED T&S UNITS, PER DRAWING SUPPLIED BY MIS. UPDATED ALL RAPP EQUIPMENT.		
	7	3A, 4C, 5A	11, TO 15	REVISED MAIN DECK ARRANGEMENT TO SUIT DRAWING SUPPLIED BY MIS. REVISED 01 DECK ARRANGEMENT TO SUIT DRAWING SUPPLIED BY MIS. UPDATED ALL RAPP EQUIPMENT.		
	8	5C	16, 17, 18	UPDATED HOLD & 1ST PLATFORM ARRANGEMENT PER OSU COMMENTS. ADDED GRATING PLATFORMS TO SCIENCE STORES, WINCH ROOM, AND MOTOR DRIVE ROOM.		
D	2	5A	1	ADDED "PERGOLA" STYLE ANTENNA SUPPORT IN LIEU OF "STAR" ARRANGEMENT.	12/27/18	MEH/CF
	3	4A	2	ADDED "PERGOLA" STYLE ANTENNA SUPPORT IN LIEU OF "STAR" ARRANGEMENT.		
	4	5A	3	ADDED "PERGOLA" STYLE ANTENNA SUPPORT IN LIEU OF "STAR" ARRANGEMENT.		
		5A	4	REVISED GRATING IN ECR.		
		5A	5	REVISED FLAT TO STOP AT FR 30.		
	5	6A,3A	6	ADDED "PERGOLA" STYLE ANTENNA SUPPORT IN LIEU OF "STAR" ARRANGEMENT.		
	7	4C,4A	7	UPDATED PORT LONG'L BHD STIFFENER THROW IWO STAIRS.		
	7	4C,4A	8	REVISED TRANSVERSE BHD AT FR 37 TO STRUCTURAL. ADDED WEATHERTIGHT DOOR FOR ACCESS INTO THE UPTAKE AT FR 50 PORT.		

REVISIONS CONTINUED

REV	SH	ZONE	ITEM	DESCRIPTION	DATE	APPVL SIG & ORG
D	9	4C	9	RELOCATED EYE WASH STATION IN WET LAB.	12/27/18	MEH/CF
		4C	10	MOVED SINK AND ADDED INDICATION OF ICE-MAKER.		
		4C	11	UPDATED GARBAGE ROOM ARRANGEMENT PER LATEST MACHINERY ARRANGEMNET.		
		4C	12	ADDED VENT TRUNK IN LOUNGE AND BOSUN STORES/SHOP.		
		4C	13	ADDED FREEING PORTS IN WET LAB.		
		4C	14	RELOCATED STERN A-FRAME TO MATCH STERN FRAME A-FRAME FDN DRAWING AND SHOWED CLEARANCE WITH VANS.		
	8	4C	15	RELOCATED SHORE POWER AND ADDED VENT ON 01 DECK AFT FR 47.		
	8	4C	16	ADDED DOOR TO FAN ROOM ON 01 DECK.		
	10	5C	17	DELETED JOINER BHD AT SIDE SHELL IN THE DATA CENTER.		
		5C	18	RELOCATED FIRE STATION AT FR 30.		
		5C	19	RELOCATED EYE WASH STATION IN SCIENCE STORES.		
		5C	20	DELETED INDICATION OF MANIFOLD IN ENGINE ROOM.		
	9	4C	21	UPDATE MAIN DECK ARRANGEMENT PER CO-018, GALLEY MESS, AND SCULLERY UPDATES	3/1/19	GM/CFF
	3,5	4A,3A	22	UPDATE MAIN DECK, AND OUTBOARD PROFILE (PORT), ADDING TRANSDUCER POLE ARRANGEMENT		
	9	4C	23	SCULLERY SINK MOVED AFT, GIVING 23" IN BETWEEN AS PER CHANGE ORDER 18.	6/11/19	AD/CF
	9	4C	24	REMOVED DRESSER IN COMPUTER LAB.		
	7	4A,4C	25	DESIGNATED STATEROOMS 02-33-2 & 02-37-02 AS 2ND ENGINEER AND 3RD ENGINEER AS FOR CHANGE ORDER 24.		
	7	4A,4C	26	DESIGNATED STATEROOMS 02-21-2 & 02-25-02 AS 2ND MATE AND 3RD MATE.		
	7	4A,4C	27	CREATED SEPARATE SHOWER AND TOILET/LAVATORY SPACES, ACCESSIBLE BY ENTRY VESTIBULE FOR AFT STATE ROOMS (02-33-2, 02-37-2).		
	7	4A,4C	28	REPLACED DECK AND WADROBE WITH SECRETARY WADROBE IN AFT STATEROOMS (02-33-2, 02-37-2)		
	7	4C	29	CREATED SEPERATEM SHOWER AND TOILET/LAVATORY SPACES, ACCESSIBLE BY ENTRY VESTIBULE FOR PORT FWD STATE ROOMS (02-21-2, 02-25-2) FOR HULLS 6096 & 6098 ONLY.		
	7	4C	30	REPLACED DECK AND WARDROBE WITH SECRETARY WARDROBE IN PORT FWD STATE ROOMS (02-21-2, 02-25-2) FOR HULLS 6096 & 6098 ONLY.		
	7	4A,4C	31	REPLACED SINGLE CHAIR WITH 2 PERSON SETTEE IN CAPTAIN CABIN.		
	7	4A,4C	32	RELOCATED FR 21 AFT JOINER BHD APPROX. 6 INCHES AFT IN CAPTAIN CABIN.		
	8	4C	33	RELOCATE FRAME 29 JOINER BHD AFT TO FRAME 40 IN HOSPITAL.		
	8	4C	34	EXTENDED AFT BHD DIAGONALLY STBD AND AFT FROM FRAME 40 TO FRAME 37 IN STATEROOM 01-34-0.		
	8	4C	35	RELOCATE FWD JOINER MBHD TO FWD SIDE OF STANCHION AT FRAME 24 IN STATEROOM 01-34-0.		
	8	4C	36	REMOVED 2 WARDROBES, REPLACED 1 WARDROBE AND DESK WITH SANCTUARY WARDROBE IN STATEROOM 01-34-0.		
	8	4C	37	MOVED BUNK TO LINE UP WITH FRAME 34 IN STATEROOM 01-34-0.		
	8	4C	38	IN PASSAGEWAY 01-15-2, RELOCATED BUBBLER TO JOINER BHD ADJACENT OF HOSPITAL ENTRY.		

PROFESSIONAL ENGINEER STAMP

OREGON STATE UNIVERSITY
CORVALLIS, OR 97331

199'-6" REGIONAL CLASS RESEARCH VESSEL

GENERAL ARRANGEMENT

GENERAL NOTES & REFERENCES

SIZE	FSCM CAGE NO.	DRAWING NO.	REV
D	7UTH5	6096-070-001	J
SCALE: NONE		HULL #: 6096 6097 6098	SHEET 1A OF 10

REVISIONS CONTINUED

REV	SH	ZONE	ITEM	DESCRIPTION	DATE	APPVL SIG & ORG
D	9	4C	39	IN LOUNGE RELOCATED JOINER BHD FROM FR 33 TO FRAME 33 ½ AS FOR CHANGE ORDER 27 FOR HULL 6096 ONLY.	6/11/19	AD/CF
	9	4C	40	IN LOUNGE RELOCATED FWD, STARBOARD BHD TO PORT TO MAINTAIN PASSAGEWAY WIDTH FOR HULL 6096 ONLY.		
	9	4C	41	DELETED 654-1 ROUND TABLE FOR HULL 6096 ONLY.		
	9	4C	42	REPLACED 600-2 PADDED ARM CHAIR WITH 3 PERSON SOFA FOR HULL 6096 ONLY.		
	9	4C	43	REPLACED 645-4 SOFA WITH 3 PERSON SOFA FOR HULL 6096 ONLY.		
	9	4C	44	DELETED 645-7 2 DRAWER FILLING CABINET FOR HULL 6096 ONLY.		
	9	4C	45	DELETED 645-6 DESK FOR HULL 6096 ONLY.		
	9	4C	46	REPLACED 640-16 BOOK SHELF WITH 72" TALL BOOKSHELF FOR HULL 6096 ONLY.		
	9	4C	47	ADDED 1 COFFEE TABLE FOR HULL 6096 ONLY.		
	9	4C	48	ADDED 1 STORAGE CABINET FOR HULL 6096 ONLY.		
	9	4C	49	DELETED HALF HEIGHT BHD IN MESS FOR HULL 6096 ONLY.		
	9	4C	50	LOCATED STRUCTURAL SANCTIONS FOR HULL 6096 ONLY.		
	9	4C	51	REMOVED BOOTH SEATING FOR HULL 6096 ONLY.		
	9	4C	52	ADDED LONG CUSHIONED BENCH SEATED ALONG OUTBOARD SHELL, ALSO REPLACED RECTANGULAR TABLES WITH LONGER TABLES WITH ROUND CORNERS FOR HULL 6096 ONLY.		
	9	4C	53	INCREASED SEATING FROM 18 TO 20 BY PROVIDING 16 SIDE CHAIRS FOR HULL 6096 ONLY.		
	9	4C	54	REARRANGED WHEEL CHAIR LOCATION FOR HULL 6096 ONLY.		
	9	4C	55	MOVED SLIDING DOORS TO FIT NEW ARRANGEMENT FOR HULL 6096 ONLY.		
D	9	4C	56	ADDED DOOR TO DC LKR.	6/19/19	AD/CF
	9	4C	57	ADDED FREEING PORT TO VESTIBULE.		
	9	4C	58	MOVED DOOR IN BOSUN STORES/SHOP 10 INCHES TOWARDS PORTSIDE.		
	9	4C	59	SHIFTED CLEAR FUEL OVERFLOW INBOARD.		
	9	4C	60	SHIFTED EYEWASH OUTBOARD.		
	10	5C,5A	61	MOVED INBOARD BHD OUTBOARD TO MATCH NEW SEACHEST ARRANGEMENT.		
	8	6A	62	REMOVED SHORE POWER LOCATION.		
E	2	6A	1	REVISED ELEVATION PER OSU COMMENTS.	8/8/19	GPM/CFF
	3	4A	2	ADDED SIDE SHELL SOCKETS, PER OSU COMMENTS.		
	4	5A	3,4	REVISED FLAG BLOCK CABLE PIPE. REVISED CENTERLINE STANCHIONS PER OSU COMMENTS		
	5	3A	5	REVISED PER OSU COMMENTS.		
	6	5C,4A	6	UPDATE EXHAUST UPTAKE VIEWS, ADDING EMERGENCY EXHAUST, AND VARIOUS VENTS.		
	8	4C	7	VERIFIED WARDROBE/SEC. WITH MARINE INTERIORS ARRANGEMENT.		
	9	4C,4A	8	REVISED PER OSU COMMENTS. ADDED PARTIAL PLAN VIEW, FOR HULL #6097, INDICATING THE FIXED PEDESTAL SEATING IN THE MESS AREA. HULL'S #6096 & 6098, WILL HAVE FOLDING CHAIRS FOR SEATING.		
	3	3B	10	REMOVED OUTBOARD PORT RUBRAIN FR56-FR67	9/12/19	KS/CFF
	9	3D,3B	11	MOVED SANCTIONS TO CORRECT LOCATION IN MESS		
	9	3C,3A	12	ADDED MISSING PORTLIGHTS TO MAIN DECK		
F	9	2D	1	UPDATED TO REFLECT CHANGE ORDER 38	9/16/19	
G	2,3	2C,7B	1	EXTENDED ANCHOR HANDLING BOLSTER TO 13'6" ABV BL	11/18/19	JGP/CFF
	4	7B	2	ADDED UNDERWATER CAMERA	1/08/2020	MJF/CFF
	10	7C,7D	2			
H	4	4C	1	UPDATED HEIGHT OF POTABLE WATER TANK	3/20/2020	JGP/CFF
	4	6C	2	REMOVED PRELIMINARY FROM CRANE		
	7	4C	3	REMOVED UPPER VIEW OF HULLS 6096 & 6098 PER CO-045		

REVISIONS CONTINUED

	7	4C	4	ADJUSTED HEAD SPACE TO ACCOMMODATE ELECTRICAL PANEL AT FR. 17		
	8	6B 6D	5	ADDED CONTAINMENT FOR VENTILATION INTAKE		
	9	2B 2C	6	REARRANGED DRY STORES TO MATCH MODEL		
	VAR	VAR	7	UPDATED RAILING ON 01 DECK		
	6	5B	8	UPDATED CHART TABLE PER CO-046		
	3 9	2B 6D	9	UPDATED TRANSDUCER POLE LOCATION PER CO-050		
J	2,3	VAR	1	UPDATED FWD MAST LIGHT.		
	4	4B	2	UPDATED POTABLE WATER TANK.		
	7	5B,4B	3	UPDATED DOORS AND BULKHEADS.		
	8	5D	4	UPDATED EQUIPMENT IN HAVC EQUIP 01-40-4.		
	10	6C	5	UPDATED W/C 3-65-1 ARRANGEMENT.		
	8	6B,6C	6	ADDED CRANE LOCAL CONTROL AND UPDATED SLEWING LOCK LOCATION.		
	10	3C	7	RELOCATED CONDUITS TO TRANSCEIVER ROOM 2-18-1.	9/1/20	KJM

PROFESSIONAL ENGINEER STAMP

OREGON STATE UNIVERSITY
CORVALLIS, OR 97331


199'-6" REGIONAL CLASS RESEARCH VESSEL

GENERAL ARRANGEMENT


GENERAL NOTES & REFERENCES

SIZE	FSCM CAGE NO.	DRAWING NO.	REV
D	7UTH5	6096-070-001	J
SCALE: NONE		HULL #: 6096 6097 6098	SHEET 1B OF 10

VESSEL PARTICULARS	
LWL	184'–0"
LOA	199'–6"
BEAM	41'–0"
HULL DEPTH	19'–0"
DESIGN DRAFT	12'–6"
AIR DRAFT (w/ANTENNAS)	76'–0"
AFT MAIN DECK W/O VANS ON DECK	1990 FT²
SIDE DECK LENGTH	79'–0"
TOTAL AFT & SIDE DECKS W/O VANS ON DECK	2220 FT²
MAIN LAB	519 FT²
WET LAB	440 FT²
COMPUTER LAB	175 FT²
DATAPRESENCE CENTER	245 FT²
SCIENCE	7 DOUBLE S/R
ACCESSIBLE SCIENCE	1 DOUBLE S/R
CREW	7 SINGLE S/R
	3 DOUBLE S/R

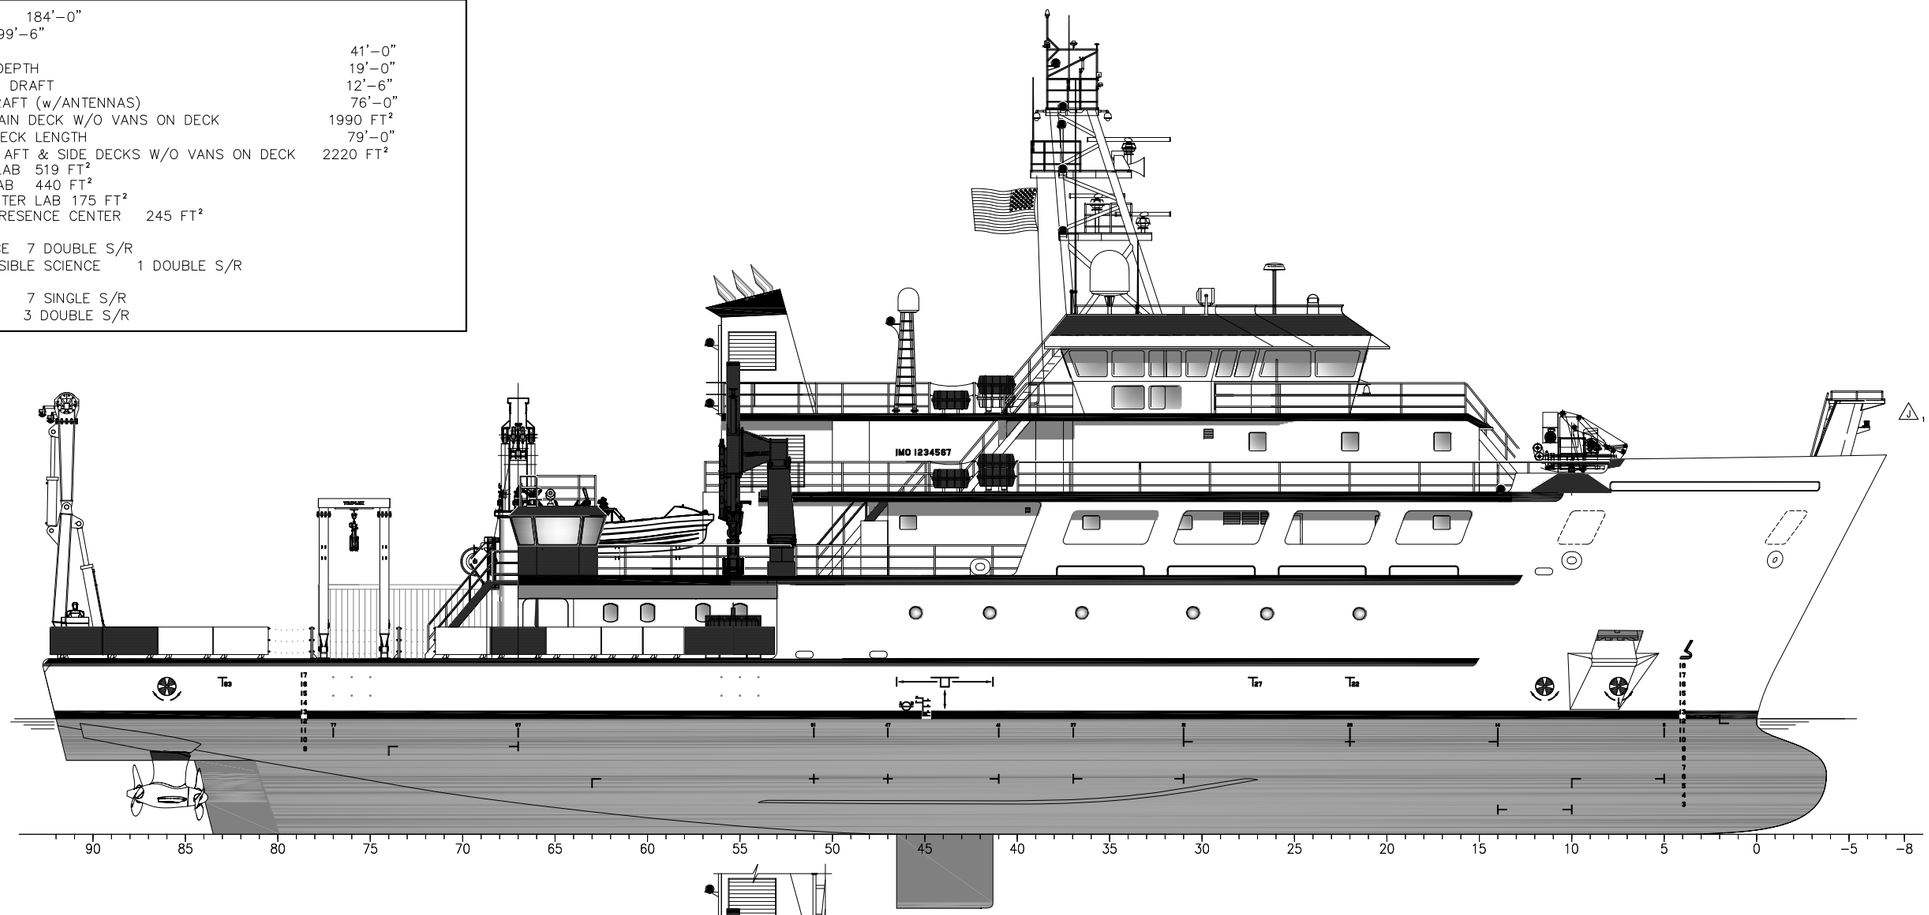

ELEVATION 2–5A
OUTBOARD PROFILE
1/8"=1'–0"

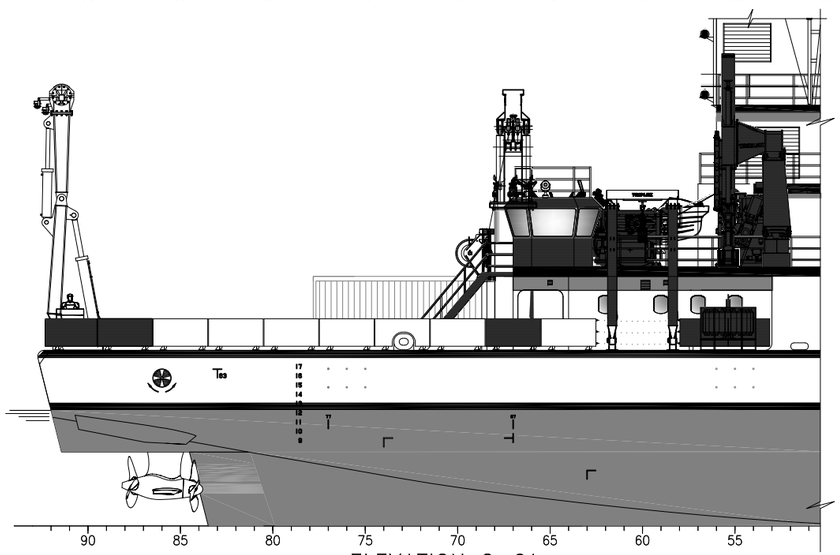

ELEVATION 2–6A
OUTBOARD PROFILE w/SIDE A–FRAME GATE OPEN
1/8"=1'–0"


PROFESSIONAL ENGINEER STAMP

OREGON STATE UNIVERSITY
CORVALLIS, OR 97331

199'–6" REGIONAL CLASS RESEARCH VESSEL

GENERAL ARRANGEMENT
ELEVATION – OUTBOARD PROFILE

SIZE	FSCM CAGE NO.	DRAWING NO.	REV
D	7UTH5	6096-070-001	J
SCALE: NONE		HULL #: 6096 6097 6098	SHEET 2 OF 10

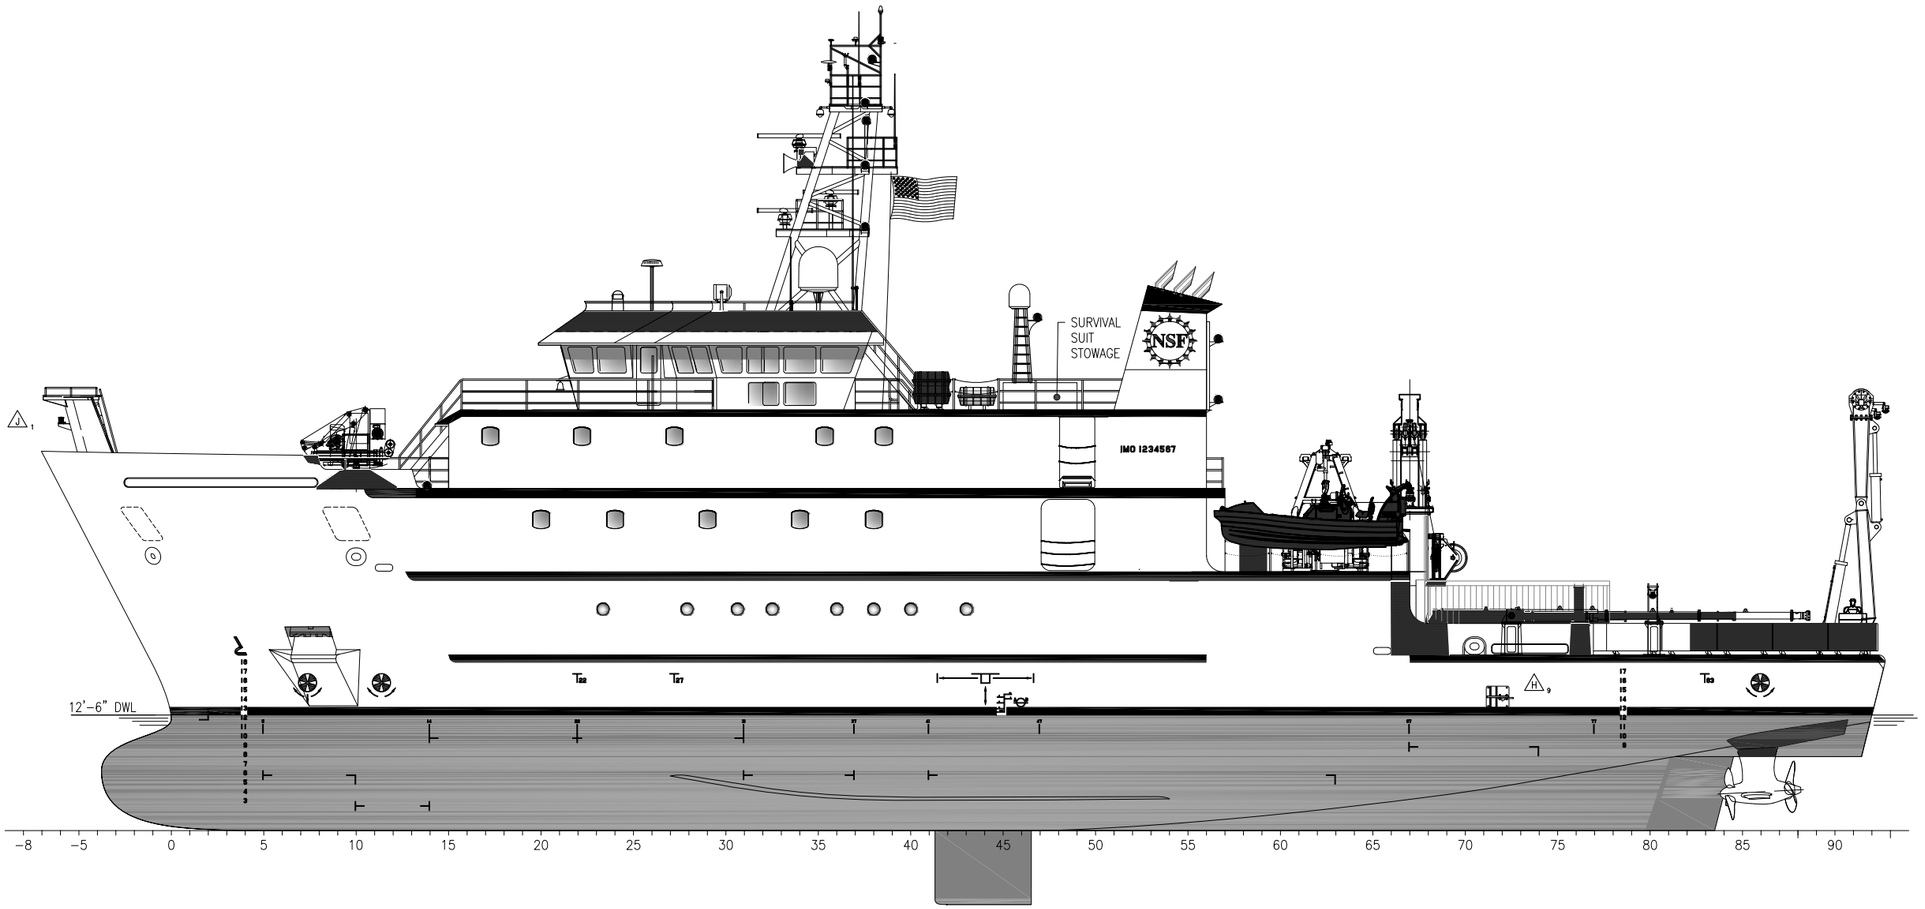

ELEVATION 3-4A
PORT OUTBOARD PROFILE
1/8"=1'-0"


PROFESSIONAL ENGINEER STAMP

OREGON STATE UNIVERSITY
CORVALLIS, OR 97331

199'-6" REGIONAL CLASS RESEARCH VESSEL

GENERAL ARRANGEMENT
ELEVATION – PORT OUTBOARD PROFILE

SIZE	FSCM CAGE NO.	DRAWING NO.	REV
D	7UTH5	6096-070-001	J
SCALE: NONE		HULL #: 6096 6097 6098	SHEET 3 OF 10

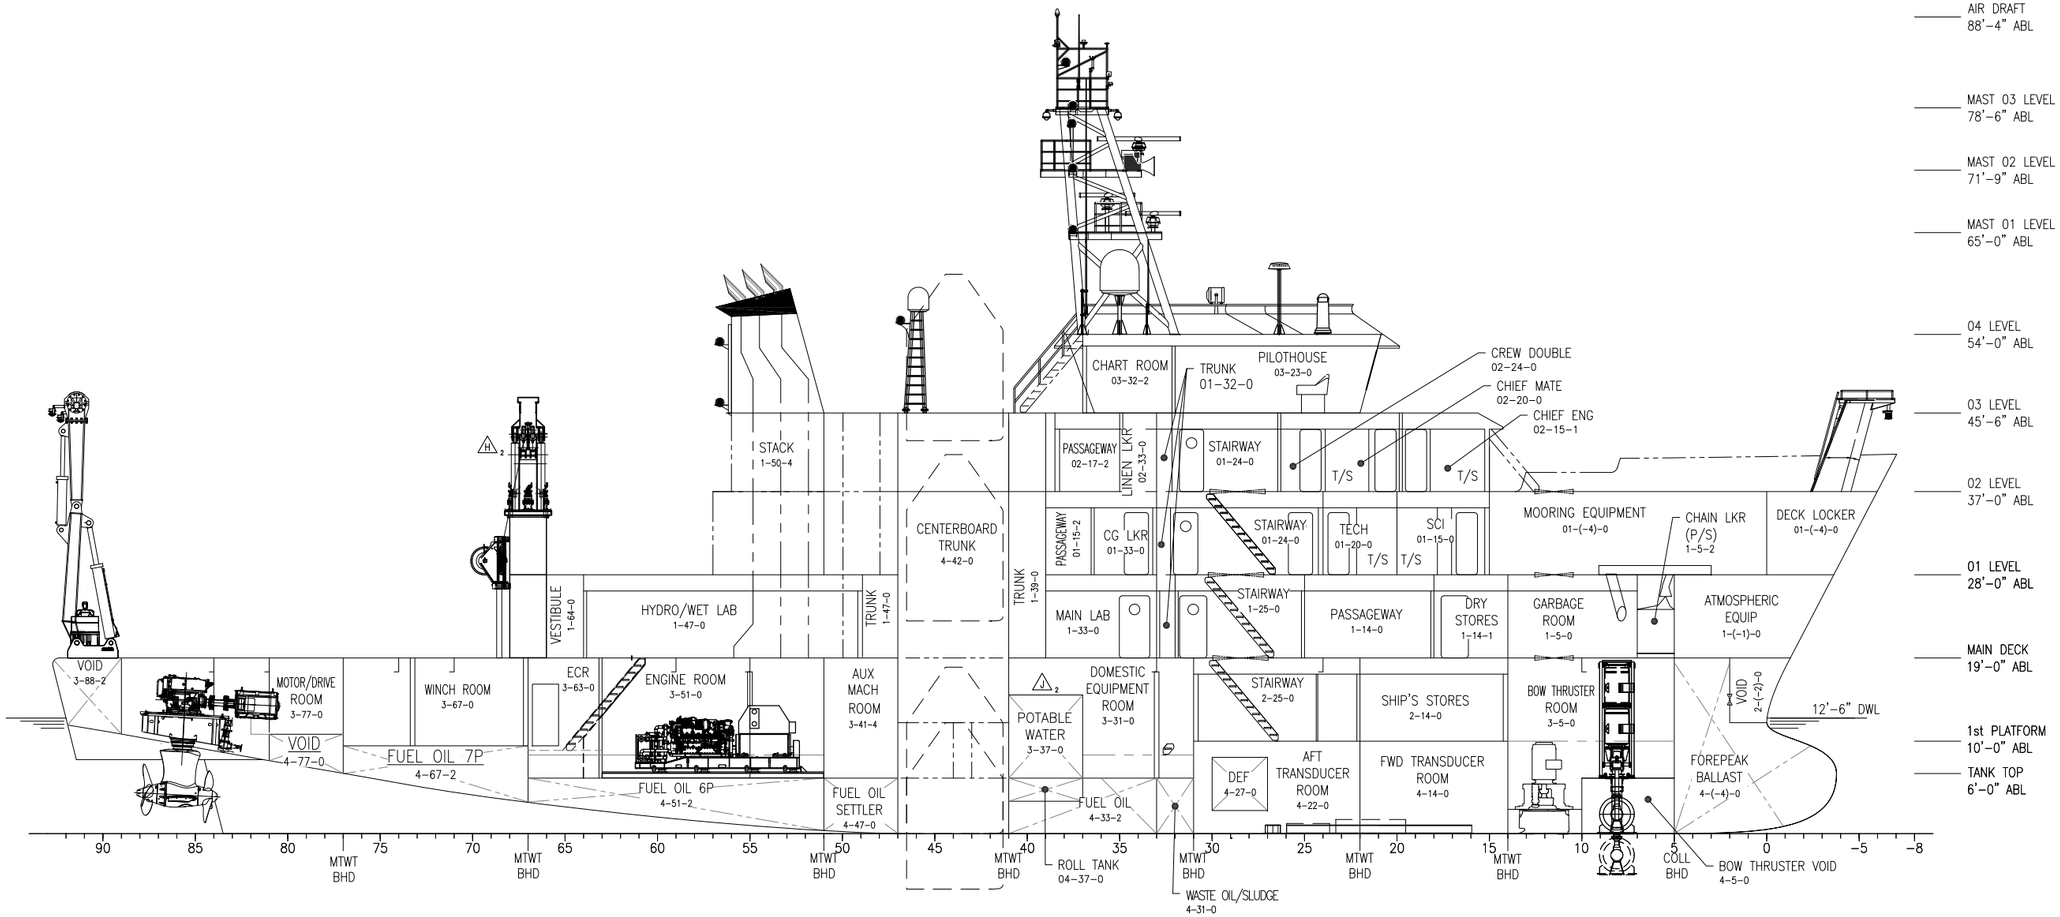

ELEVATION 4-5A

INBOARD PROFILE

1/8"=1'-0"

PROFESSIONAL ENGINEER STAMP

OREGON STATE UNIVERSITY
CORVALLIS, OR 97331


199'-6" REGIONAL CLASS RESEARCH VESSEL

GENERAL ARRANGEMENT


ELEVATION – INBOARD PROFILE

SIZE	FSCM CAGE NO.	DRAWING NO.	REV
D	7UTH5	6096-070-001	J

SCALE: NONE | HULL #: 6096 6097 6098 | SHEET 4 OF 10

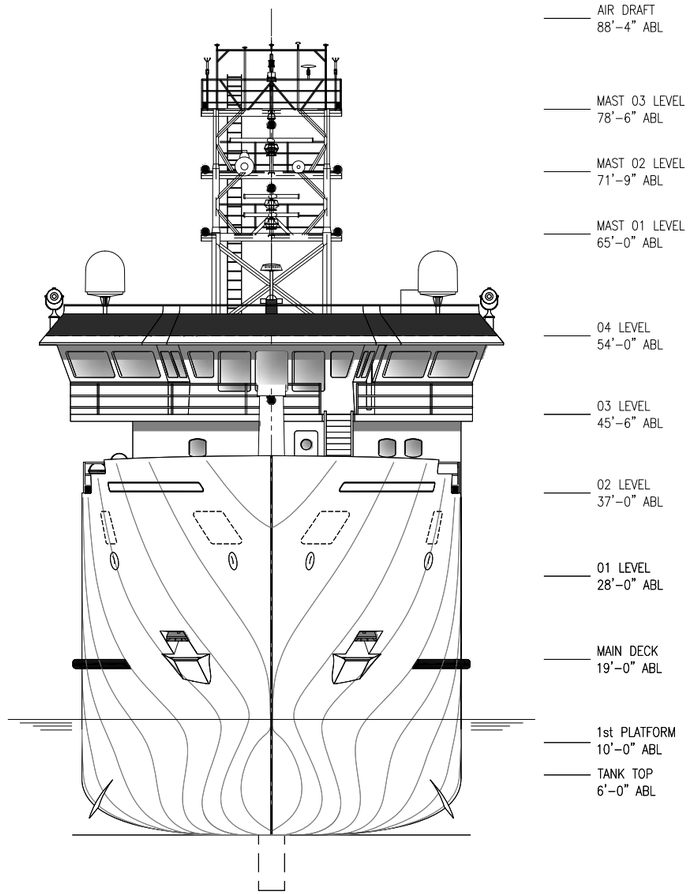

SECTION 5-6A
LOOKING AFT
1/8"=1'-0"

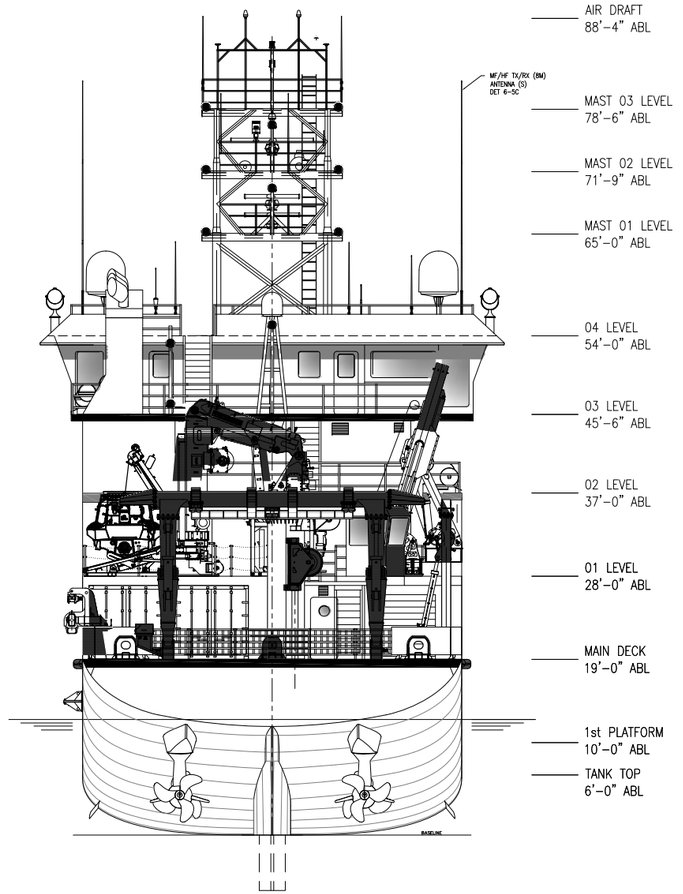

SECTION 5-3A
LOOKING FWD
1/8"=1'-0"


PROFESSIONAL ENGINEER STAMP

OREGON STATE UNIVERSITY
CORVALLIS, OR 97331

199'-6" REGIONAL CLASS RESEARCH VESSEL

GENERAL ARRANGEMENT
SECTION - END VIEWS


SIZE	FSCM CAGE NO.	DRAWING NO.	REV
D	7UTH5	6096-070-001	J
SCALE: NONE		HULL #: 6096 6097 6098	SHEET 5 OF 10

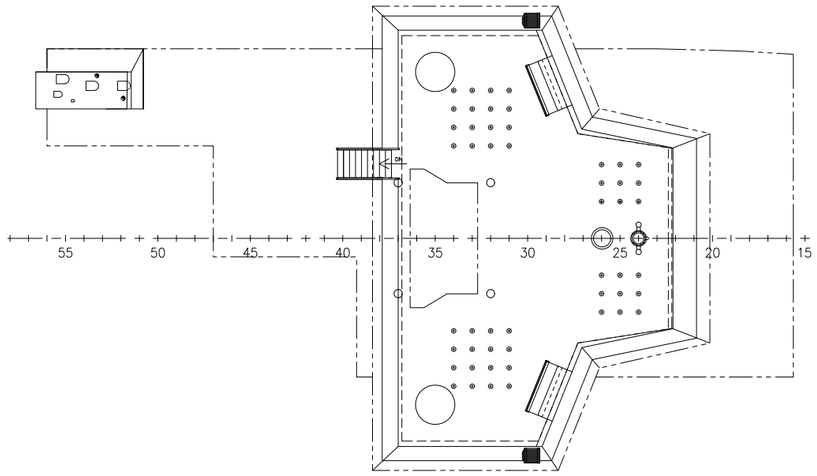

PLAN 6–5C

04 LEVEL (PILOTHOUSE TOP)

1/8"=1'–0"

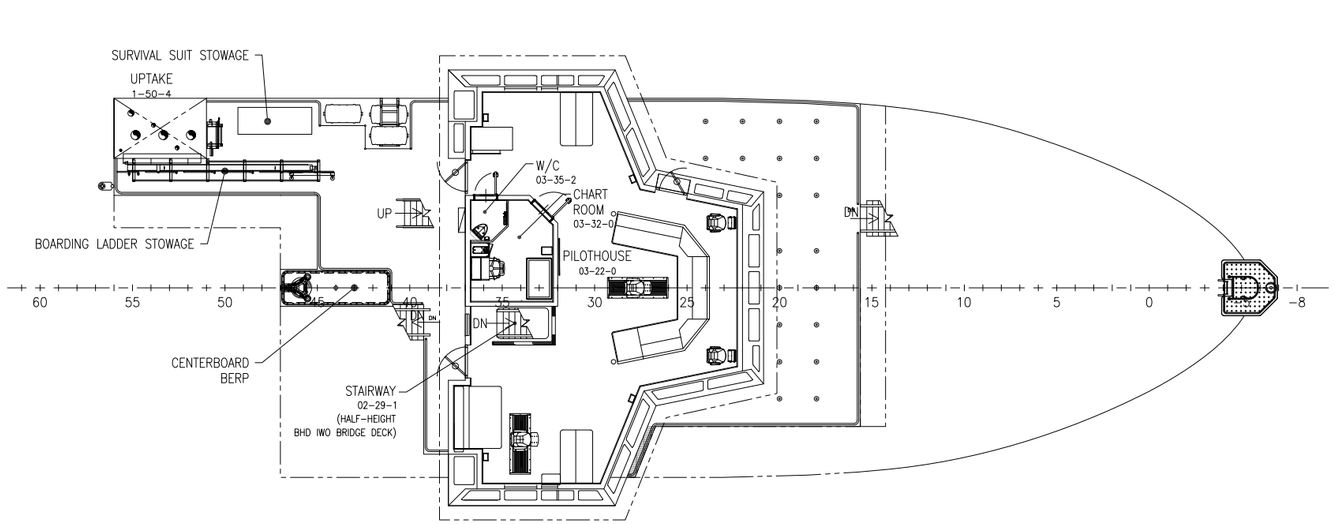

PLAN 6–4A

03 LEVEL (PILOTHOUSE)

1/8"=1'–0"

PROFESSIONAL ENGINEER STAMP


OREGON STATE UNIVERSITY
CORVALLIS, OR 97331

199'–6" REGIONAL CLASS RESEARCH VESSEL

GENERAL ARRANGEMENT

PLAN VIEW – 02, 03, & 04 LEVEL

SIZE	FSCM CAGE NO.	DRAWING NO.	REV
D	7UTH5	6096–070–001	J
SCALE: NONE		HULL #: 6096 6097 6098	SHEET 6 OF 10

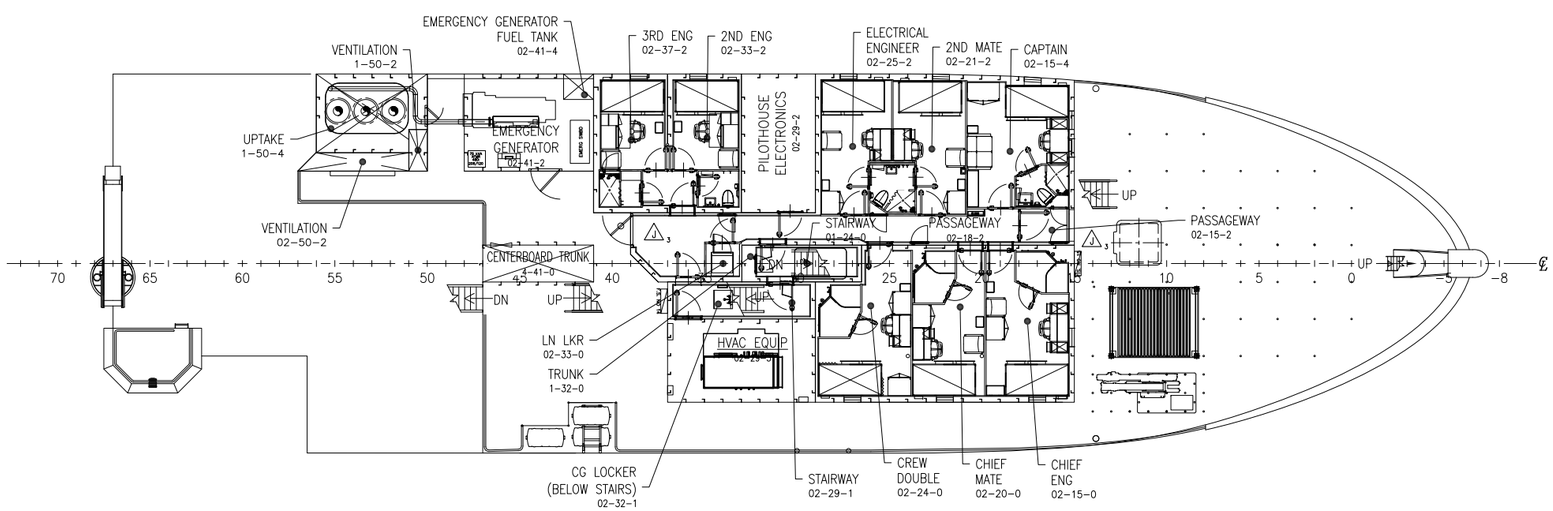

PLAN 7-4A

02 LEVEL

1/8"=1'-0"

PROFESSIONAL ENGINEER STAMP

OREGON STATE UNIVERSITY


CORVALLIS, OR 97331

199'-6" REGIONAL CLASS RESEARCH VESSEL

GENERAL ARRANGEMENT

PLAN VIEW – 02, 03, & 04 LEVEL


SIZE	FSCM CAGE NO.	DRAWING NO.	REV
D	7UTH5	6096-070-001	J
SCALE: NONE		HULL #: 6096 6097 6098	SHEET 7 OF 10

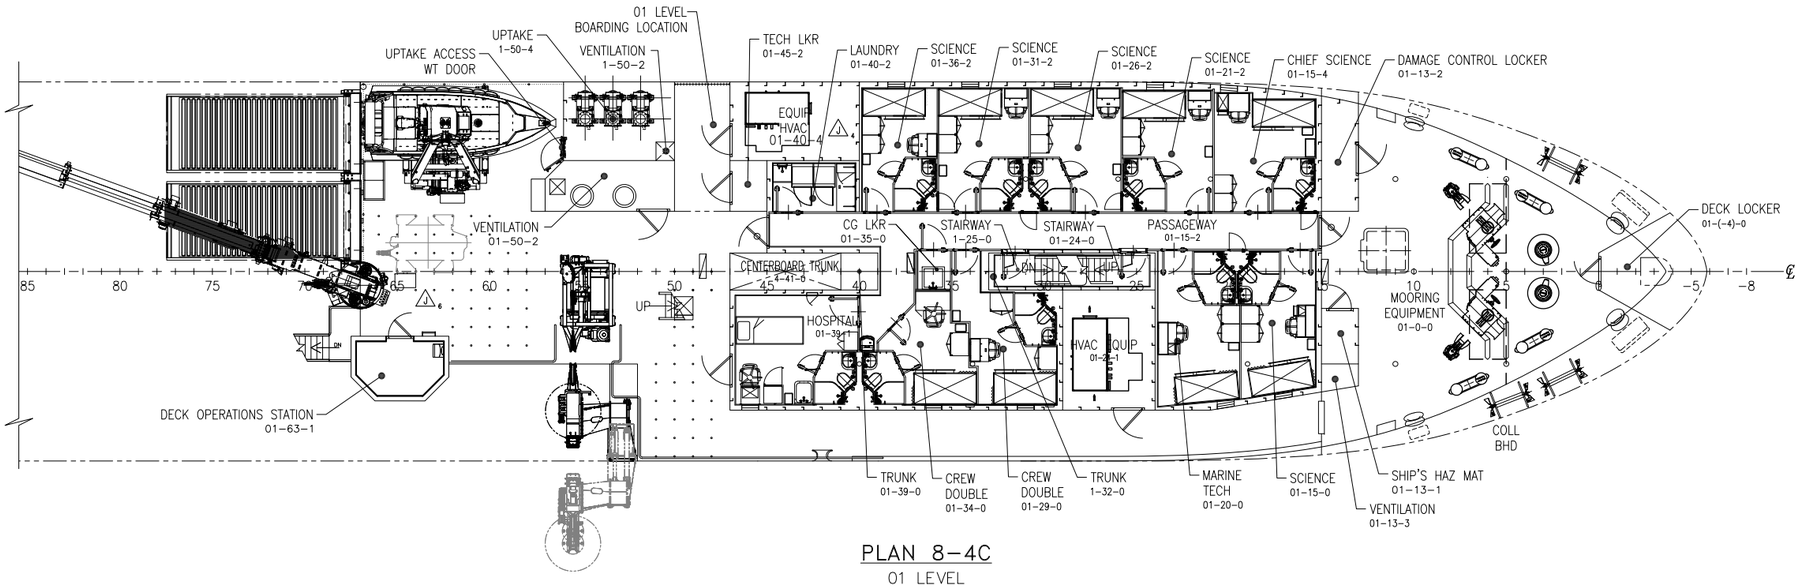

PLAN 8-4C

01 LEVEL

1/8"=1'-0"

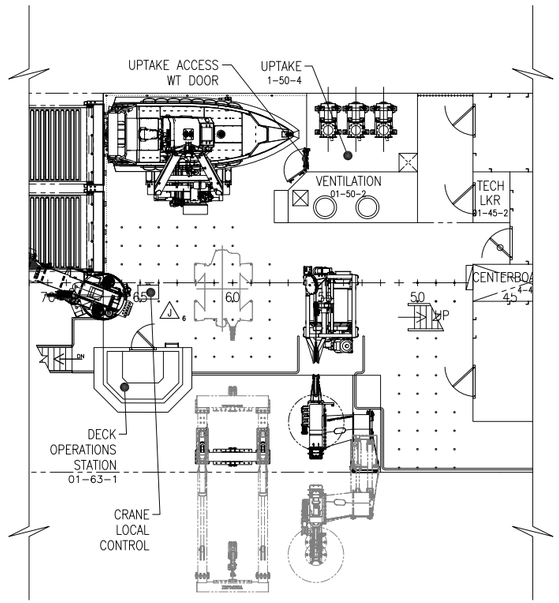

PLAN 8-6A

01 LEVEL, ALTERNATE WINCH DECK

1/8"=1'-0"

PROFESSIONAL ENGINEER STAMP


OREGON STATE UNIVERSITY
CORVALLIS, OR 97331

199'-6" REGIONAL CLASS RESEARCH VESSEL

GENERAL ARRANGEMENT

PLAN VIEW – MAIN DECK & 01 LEVEL

SIZE	FSCM CAGE NO.	DRAWING NO.	REV
D	7UTH5	6096-070-001	J
SCALE: NONE		HULL #: 6096 6097 6098	SHEET 8 OF 10

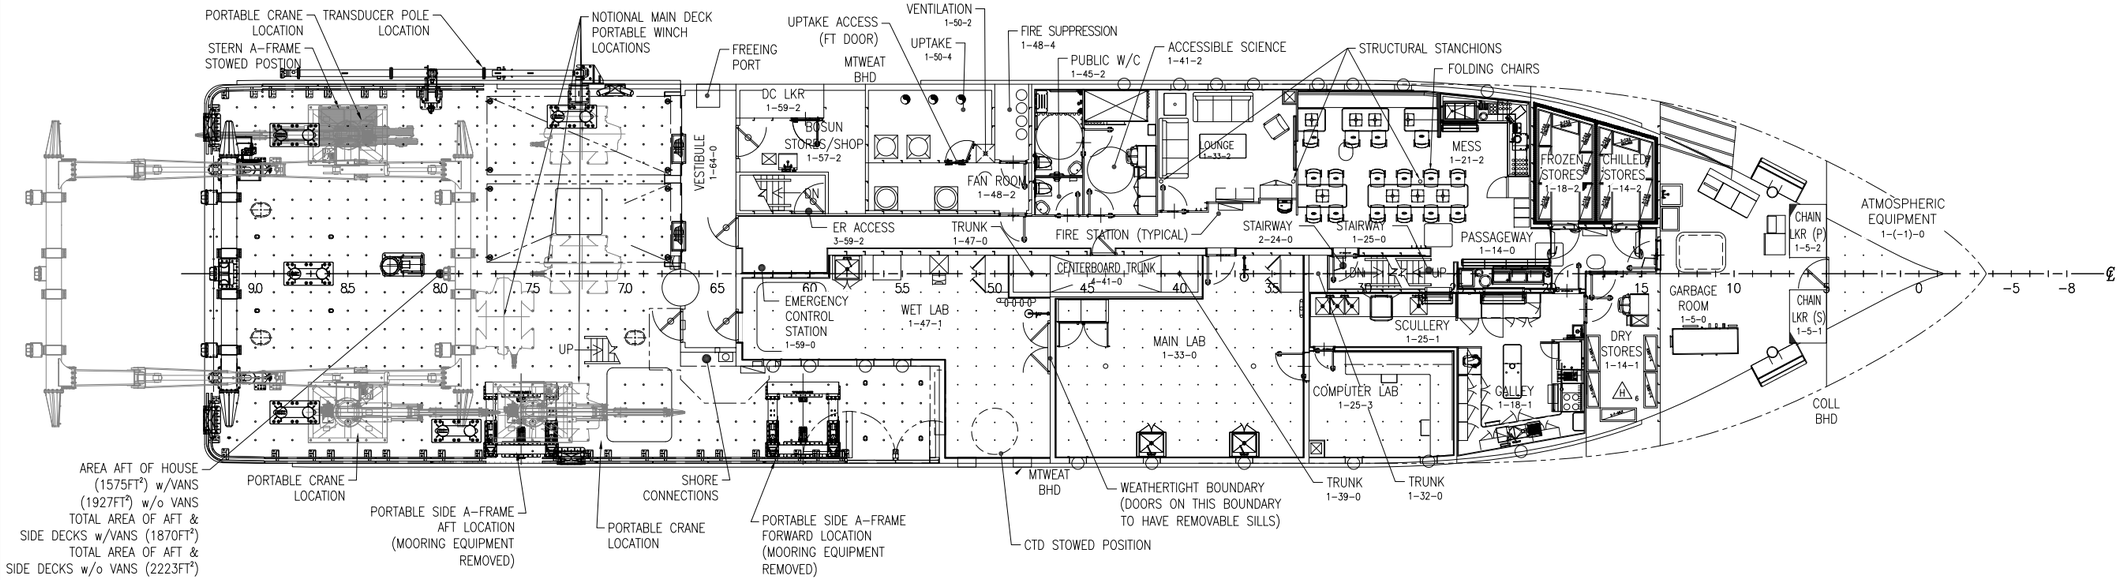


PLAN 9-4C

MAIN DECK

HULL 6096 & 6098

1/8"=1'-0"

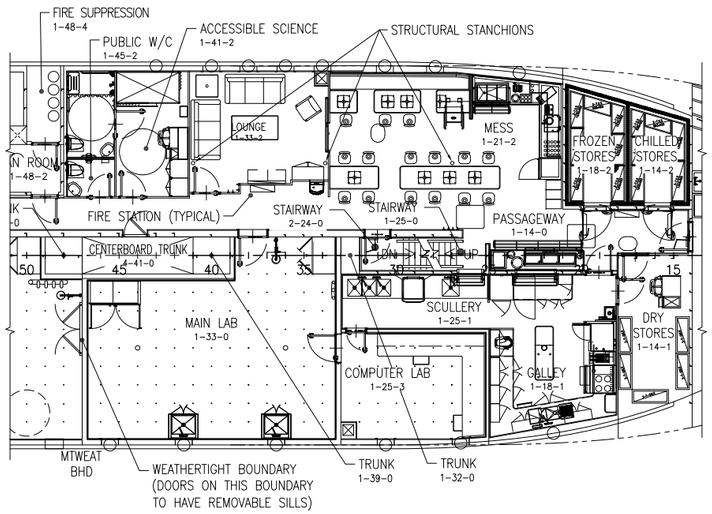

PLAN 9-4A

MAIN DECK

HULL 6097

1/8"=1'-0"

PROFESSIONAL ENGINEER STAMP

OREGON STATE UNIVERSITY
CORVALLIS, OR 97331


199'-6" REGIONAL CLASS RESEARCH VESSEL

GENERAL ARRANGEMENT

PLAN VIEW – MAIN DECK & 01 LEVEL

SIZE	FSCM CAGE NO.	DRAWING NO.	REV
D	7UTH5	6096-070-001	J
SCALE: NONE		HULL #: 6096 6097 6098	SHEET 9 OF 10


Fine | Not fine | Cannot determine

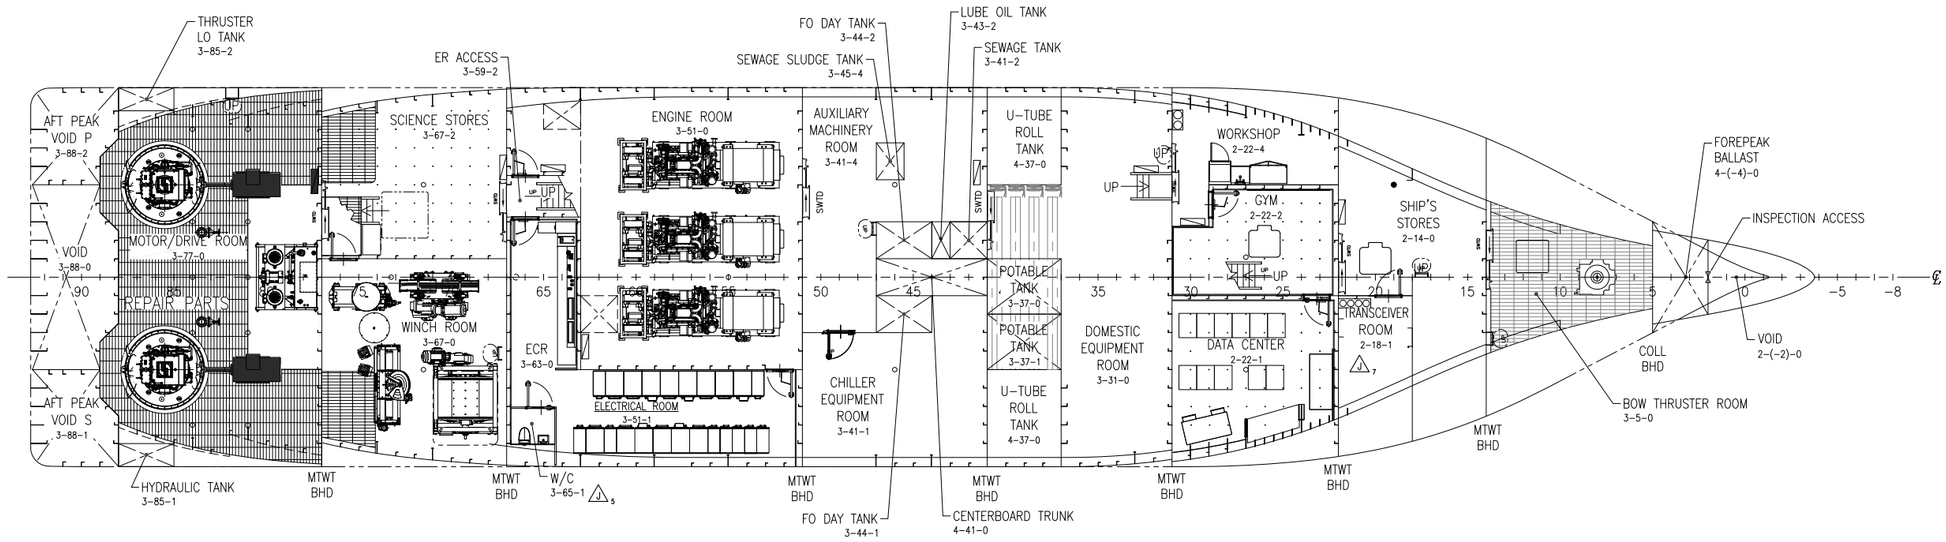

PLAN 10–5C

HOLD & 1ST PLATFORM DECKS

1/8"=1'–0"

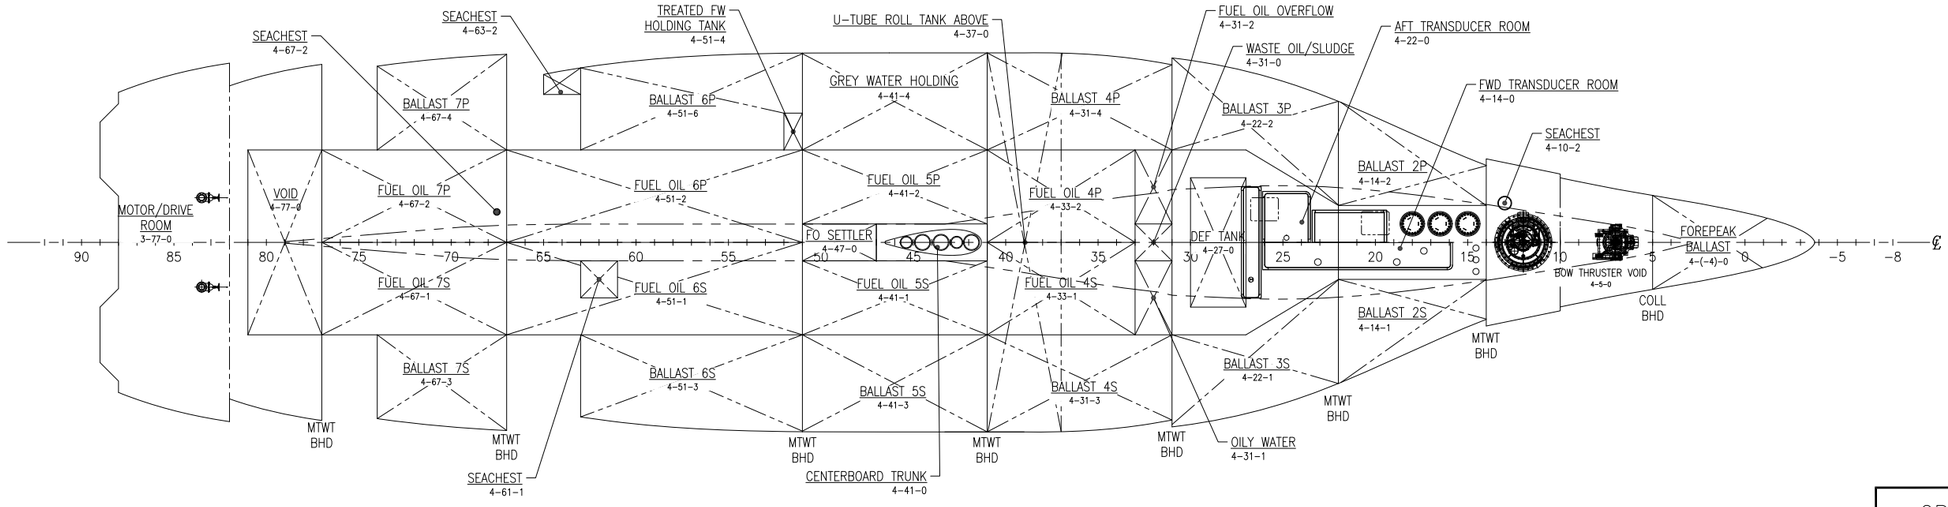

PLAN 10–5A

TANK TOP

1/8"=1'–0"

PROFESSIONAL ENGINEER STAMP

OREGON STATE UNIVERSITY
CORVALLIS, OR 97331

199'–6" REGIONAL CLASS RESEARCH VESSEL

GENERAL ARRANGEMENT

PLAN VIEW – TANK TOP, HOLD & 1ST PLATFORM

SIZE	FSCM CAGE NO.	DRAWING NO.	REV
D	7UTH5	6096-070-001	J
SCALE: NONE		HULL #: 6096 6097 6098	SHEET 10 OF 10
